



OFFICE OF THE SECRETARY TO GOVERNMENT OF THE FEDERATION

PRESENTS

**THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE
FEDERAL EXECUTIVE COUNCIL (FEC)**

FROM

MAY 2015 TO DECEMBER 2017

BY BOSS MUSTAPHA



CONTENT

1.0 INTRODUCTION

Vision, Mission Statements and Core Mandate

2.0 IMPLEMENTATION OF FEDERAL EXECUTIVE COUNCIL (FEC) APPROVALS FOR:

2.1 Ecological Fund Office

2.2 Cabinet Affairs Office

2.3 Federal Road Safety Corps

2.4 National Hajj Commission of Nigeria

2.5. National Pension Commission

2.6 National Population Commission

2.7 Economic and Financial Crimes Commission



1.0

INTRODUCTION

The Office of the Secretary to the Government of the Federation is the Secretariat of the Presidency responsible for ensuring the effective co-ordination and monitoring of the implementation of Government policies and programmes.

MANDATE

Monitor and Coordinate the implementation of Government Policies and Programmes; Serve as frontline advisory institution of the Presidency; Drive Policy formulation, harmonization, and implementation; and Monitor institutions of governance.

VISION

To lead and serve as an effective engine room for policy formulation, harmonisation, implementation and monitoring of the institutions of governance.

MISSION

To deploy political will, administrative expertise, professionalism and the values of loyalty and commitment in support of the attainment of the goals of the Federal Government.

**THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC)
FROM MAY 2015 TO DECEMBER 2017**

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
1	Reconstruction of Yola-Mubi Bridge at Kaa'a Shiwa and Mail 30 - Kwambila Road, Adamawa State	November, 2015	Ecological Fund Office	7 Months	N/A	100%	38	The Scope of work include: Site clearing /earth work; Removal of Weak structures/old bridge; Construction of Culverts; Re-construction of bridge and Construction of mile 30 - Kwambila Road. The project is 100% completed. Commissioned and handed over.
2	Daura Township Erosion Control, Phase I, Daura, Katsina State	December, 2015	Ecological Fund Office	9 Months	N/A	100%	38	The Scope of work include: Construction of Concrete Channels; Construction of Box Culverts; Stone-Pitching and Rock Dumps for each erosion Control works. The project is 100% completed. Commissioned and handed over.
3	Daura Township Erosion And Flood Control Project, Phase II, Katsina State	December, 2015	Ecological Fund Office	11 Months	N/A	100%	45	The Scope of work include: Site clearing; Construction of Culverts and Drains; and completion of Dam's accessories. The project is 100% completed. Commissioned and handed over.
4	Kaltungo Gully Erosion Control Works, Gombe State	December, 2015	Ecological Fund Office	12 Months	N/A	100%	38	The Scope of work include: Site Clearing; Drains of various sizes & dimension in different locations in the town including Culverts and 5km Road improvement. The project is 100% completed. Awaiting commissioning and handing over.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
5	Gully Erosion Control Works at Veritas University, Bwari, Abuja.	December, 2015	Ecological Fund Office	7 Months	N/A	100%	38	The Scope of work include: Site Clearing; Construction of Culverts; and road improvement. The project is 100% completed. Awaiting commissioning and handing over.
6	Kwoi Erosion and Flood Control Project at Jaba, Kaduna State	February, 2017	Ecological Fund Office	10 Months	N/A	100%	40	The Scope of work include: (i) Site Clearing (ii) Earth work (iii) 1.5km Road Improvement; (iv) 5 Nos. Culverts and 725m of Drainages of various dimensions . The project is 100% completed and awaiting commissioning and handing over.
7	Remediation of Warri Refinery Phase II, Delta State	February 2017	Ecological Fund Office	12 Months	N/A	100%	45	The Scope of works include: i. Grubbing of the mapped site; ii. Excavation of the mapped site; iii. Oily Sludge treatment under aquatic condition and clean up; iv. Site construction; v. Bio-remediation of the to its natural state; and vi. Restoration of the air quality free of hydrocarbon odour. Project is 100% completed and awaiting commissioning and handing over.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
8	Channelization and Desilting of Ogbagba and Okoko Rivers in Osogbo Phase I&II, Osun State	March, 2017	Ecological Fund Office	12 Months	N/A	100%	45	Construction of 1.2km Drainage and Channilization. Other scope includes Construction of 2 Culverts and sand filling. 100% Completed. Awaiting commissioning and handing over.
9	Mubi Flood/ Erosion Control Works and River Yalzaram Training, Phase I Adamawa State	March, 2017	Ecological Fund Office	11 Months	N/A	80%	45	The Scope of work include: (i) Clear areas for access to all locations, remote all grass and tree within the 1 No. Canal (ii) Remove Top soil up to a depth not exceeding 250mm in soft soil for all drains, outlets structure or as may be redirected by Engineers; The Status is 80% and it is on-going; Challenge: Work was suspended at site by Contractor during the raining season due to heavy downpour. However, the Contractor is back on Site and work is progressing.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
10	Erosion Control Works at Nda, Nnobi and Agbor, Idemili LGA, Anambra State	March, 2017	Ecological Fund Office	7 Months	N/A	90%	38	The scope of work include: i. Earth works; ii. Concrete drains; iii. Construction of culverts; iv. Pavement/Surfacing. The project is 90% and work is on-going. Challenge: The progress of the project was slow due to communal issues which has been taken care of.
11	Adiabo Okutikang Beach Gully Erosion Control Works, Cross River State	March, 2017	Ecological Fund Office	14 Months	N/A	90%	40	The Scope of work include: (i) Dredging of the River (2,1km) length (ii) De-silting of the River Channel (iii) Construction of 2.75km embankment. The Status is 90% and it is on-going. Challenge: Contractor not moving with the timeline and has received two warnings. However, the Contractor is back on site and work is progressing.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
12	Erosion/Flood Control Project of Rice Field, Bagudu LGA, Kebbi State	March, 2017	Ecological Fund Office	12 Months	N/A	50%	45	<p>The Scope of work include:</p> <ul style="list-style-type: none"> (i) Clear areas for access to all locations, remove all grass and tree within the canal (ii) Remove Top soil up to a depth not exceeding 250mm in soft; (iii) Construction of 1.2km Access Road. <p>The Status is 50% and it is on-going. Challenge: Contractor is not moving according to timeline and consequently has been written two letters of warning in July, 2017 and January, 2018 respectively.</p>

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	& PROCUREMENT DURATION	ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
13	Erosion/Flood Control Project of Rice Field, Suru LGA, Kebbi State	March, 2017	Ecological Fund Office	15 Months	N/A	50%	45	The Scope of work include: (i) Dam/Dyke Construction; (ii) Spillway, Stilling Basin and Bottom outlet; (iii) 5 Nos Reinforced concrete Culverts construction; (iv) Canal Construction. The Status is 40% and it is On-going. Challenge: The flood from River Niger due to heavy downpour at the peak of raining season forced the Contractor to suspend works at site for about 3 months. the Contractor is back on site and has submitted a new work plan which is still within the project time frame.
14	Sabke/Dutsi and Mashi Water Supply Project, Katsina State	March, 2017	Fed. Min. of Water Resources	19 Months	N/A	70%	45	The Scope of works include: i. Rehabilitation of Sabke Treatment Plant; ii. Completion of Distribution Network (Reticulation); iii. Completion of Dutsi Water Supply and Irrigation Plant; iv. Completion of Mashi Water Supply and Irrigation Plant; and v. Associated Works. The Project is 59.9% On-going.
15	Ecological Challenges at Alex Ekwueme University, Ndufu Alike Ikwo, Ebonyi State	April, 2017	Ecological Fund Office	8 Months	N/A	100%	45	The Scope of work include: (i) Site clearance Work; (ii) 2 Nos. Culvert and 850m length of Drains; (iii) 2.7km Pavement and Surfacing . The project is 100% completed. Awaiting Commissioning and Handing Over.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
16	Gully Erosion Control and Flood Improvement Works at Awlaw, Oji-River LGA, Enugu State	April, 2017	Ecological Fund Office	10 Months	N/A	100%	40	The Scope of work include: (i) Site clearance Work; (ii) Rehabilitation of 2.9km Access Road and Drains . The Status is 100% completed. Awaiting commissioning and handing over
17	Rijau, Dugge, Dukku, T/Magajiya and Genu, Rijau Local Government Erosion and Flood Control Project, Niger State	April, 2017	Ecological Fund Office	12 Months	N/A	100%	38	The Scope of work include: (i) Site Clearance and Earthworks; (ii) 5 Nos. Culverts and 950m length of drains; (iii) Pavement and surfacing The Status is 100% completed. It is yet to be commissioned and handed over.
18	Erosion Control Works at Odo Alaamo, Ogbomoso, Oyo State	April, 2017	Ecological Fund Office	10 Months	N/A	100%	40	The scope of work include: . i. Site Clearance; ii. Earthworks and Excavation; iii. Construction of Concrete Drains and Culverts; and iv. Road work and Pavement Construction. The project is 100% completed and awaiting commissioning and handing over.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
19	Erosion Control on the Drainage Basin of Ahmadu Bello University, Zaria Lake/Dam, Kaduna State	April, 2017	Ecological Fund Office	8 Months	N/A	95%	38	The Scope of work include: (i) Site Clearance; (ii) Construction of 150m Spillway; (iii) Desilting of reservoir; (iv) Reinstatement of Dam Embankment; (v) Provision of 275m Toe Drain; (vi) Provision of intake structure. The Status is 95% and it is on-going.
20	Nkari Erosion Control and Road Improvement Works, Ini LGA, Akwa Ibom State	April, 2017	Ecological Fund Office	9 Months	N/A	72%	40	The Scope of work include: (i) Site clearance Work; (ii) Rehabilitation of 2.5km Access Road and Drains . The Status is 72% and it is on-going. Communal clashes slowed down the progress of work.
21	Gully Erosion and Road Improvement Works, Nasarawa Town (Phase I), Nasarawa State	April, 2017	Ecological Fund Office	10 Months	N/A	80%	40	The Scope of work include: (i) Construction of Drains for flood and racketed structures (800m) (ii) 1.3km Road Improvement Works . The Status is 80% completed and it is on-going.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
22	University of Calabar Erosion & Flood Control Works, Calabar, Cross River State	May, 2017	Ecological Fund Office	9 Months	N/A	100%	38	The Scope of work include: (i) Site clearance Work; (ii) Concrete Work. (iii) Construction of 1,283m reinforced Concrete drainage; (iv) Construction of 6 Nos. Concrete catchment pit. The Status is 100% completed. Awaiting commissioning and handing over.
23	Erosion Control Project at State House Presidential Villa, Abuja	June, 2017	Ecological Fund Office	6 Months	N/A	85%	38	The Scope of work include: (i) Clearance and Fumigation; (ii) Shaping and compaction of cleared section; (iii) Reclamation of eroded section; (iv) Construction of draining and chambers; (v) Construction of 350m length Retaining walls (vi) Embankment of protection chutes, stone pitching. The Status is 70% and it is on-going. Challenge: The Security clearance from State House delayed the early commencement of the project.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
24	Flood And Erosion Control Of Damaturu-Balmari-Gashua Road, Damaturu LGA, Yobe State	June 2017	Ecological Fund Office	9 Months	N/A	50%	45	The Scope of work include: (i) Excavation (ii) 7,250m Concrete Drains and 7 Nos. of Culvert . The Status is 50% and it is on-going.
25	Ondo Township Erosion Control Works, Ondo State	November, 2017	Ecological Fund Office	9 Months	N/A	Contractor Mobilized	40	The Scope of work include: (i) Site Clearance and Earthworks; (ii) Culverts and drains; (iii) Pavement and surfacing. Construction work is on-going. The project is 15% Ongoing.
26	Erosion Control and Road Improvement Works of OORA/AAYO River, Oke-Ayo Area, Ilesha, Osun State	November, 2017	Ecological Fund Office	9 Months	N/A	45%	40	The Scope of work include: (i) Site clearing Work; (ii) Culvert and Drains; (iii) Pavement and Surfacing . Construction work is on-going. The project is 45% Ongoing.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
27	Project Development Institute Enugu (PRODA) Federal Ministry of Science & Technology, Enugu State	November, 2017	Ecological Fund Office	8 Months	N/A	50%	40	The Scope of work include: (i) Excavation (ii) 765m Concrete Drains and 5 Nos. Culvert. Construction work is on-going. The project is 50% Ongoing.
28	Gandu, Tukuntawa and Zoo Road Erosion and Flood Control Project, Kano State	November, 2017	Ecological Fund Office	6 Months	N/A	Contractor Mobilized	40	The Scope of work include: (i) Site clearance and earth work (ii) Culverts and drains; (iii) Pavement and surfacing. The project is 15% Ongoing.

ECOLOGICAL FUND OFFICE

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
29	Tundun Magayaki/Cemetery/ Gully Erosion and Flood Control, Sokoto South LGA, Sokoto State	November, 2017	Ecological Fund Office	6 Months	N/A	Contractor Mobilized	40	The Scope of work include: (i)Construction of Old Cemetery Drains; (ii)Construction of new Cemetery Drains; (iii) Construction of Drains along Dallatu Road. (iv)Repair to completed section of main drain; (v)Extending of drains from other roads to main drains Construction of main drain at Magayaki, The project is 15% Ongoing.
30	Shoreline Protection, Alebiri, Bayelsa State	November, 2017	Ecological Fund Office	8 Months	N/A	70%	45	The Scope of work include: i. 100m Shoreline protection; and ii sand filling. Dredging Machine moved to site and work has began in earnest. The project is 70% Ongoing.

ECOLOGICAL FUND OFFICE (EFO) PROJECTS BELOW FEDERAL EXECUTIVE COUNCIL (FEC) THRESHHOLD FROM MAY 2015 TO DECEMBER 2017 ARE IN ANNEX (I)

Total Numbers of Projects :	64
Numbers of Completed Projects:	55
Numbers of Ongoing Projects:	9

JOB CREATION

➤ Skilled Jobs	357
➤ Unskilled Jobs	1,350

ESTIMATED NUMBER OF JOBS CREATED BY EFO PROJECTS FROM MAY 2015 TO DECEMBER 2017

- Though the projects are short termed but during the period, several jobs were created
- The following are the types of Skilled and Unskilled Employees employed by Contractors/Consultants;

Skilled

- Civil Engineers
- Structural Engineers
- Highway Engineers
- Water Engineers
- Mechanical/Electrical Engineers
- Technicians
- Welders
- Carpenters
- Masons
- Painters

Unskilled Labourers

- In addition, these projects also impacted lives in the Communities in many ways;
 - Increase in economic productivity
 - Safety of lives and properties
 - Improvement in the standard of living
 - Access to Farmlands and Markets
 - Reduction in prices of food items
 - Increased Inter-Communal relationship and peace
 - Reduction in cost of transportation
 - Federal Government's presence being felt
 - Improved security within the Communities
 - Value of properties improved/enhanced
 - Communities have extended appreciation to Federal Government

- For Small and Medium size projects, about 90 lives are impacted which translate to about 5,760 lives in 64 projects executed

- For Bigger projects, about 120 lives are impacted which translate to about 3,600 lives in 30 projects executed


- About 8,820 lives were directly impacted and empowered

ESTIMATED NUMBER OF JOBS CREATED BY EFO PROJECTS FROM MAY 2015 TO DECEMBER 2017

- Out of 64 projects which fall within the EFO Tenders Board approval limit, about 357 skilled employees were engaged
- The Unskilled labours were about 1,409 Labourers
- Out of 30 projects which fall within the Federal Executive Council (FEC) approval, 270 skilled employees were engaged
The Unskilled labour were about 1,350
- 3,386 Professionals and Unskilled labour were created

ESTIMATED NUMBER OF JOBS CREATED BY EFO PROJECTS FROM MAY 2015 TO DECEMBER 2017

Nos of Jobs Created by EFO Projects from May, 2015 to Dec., 2017

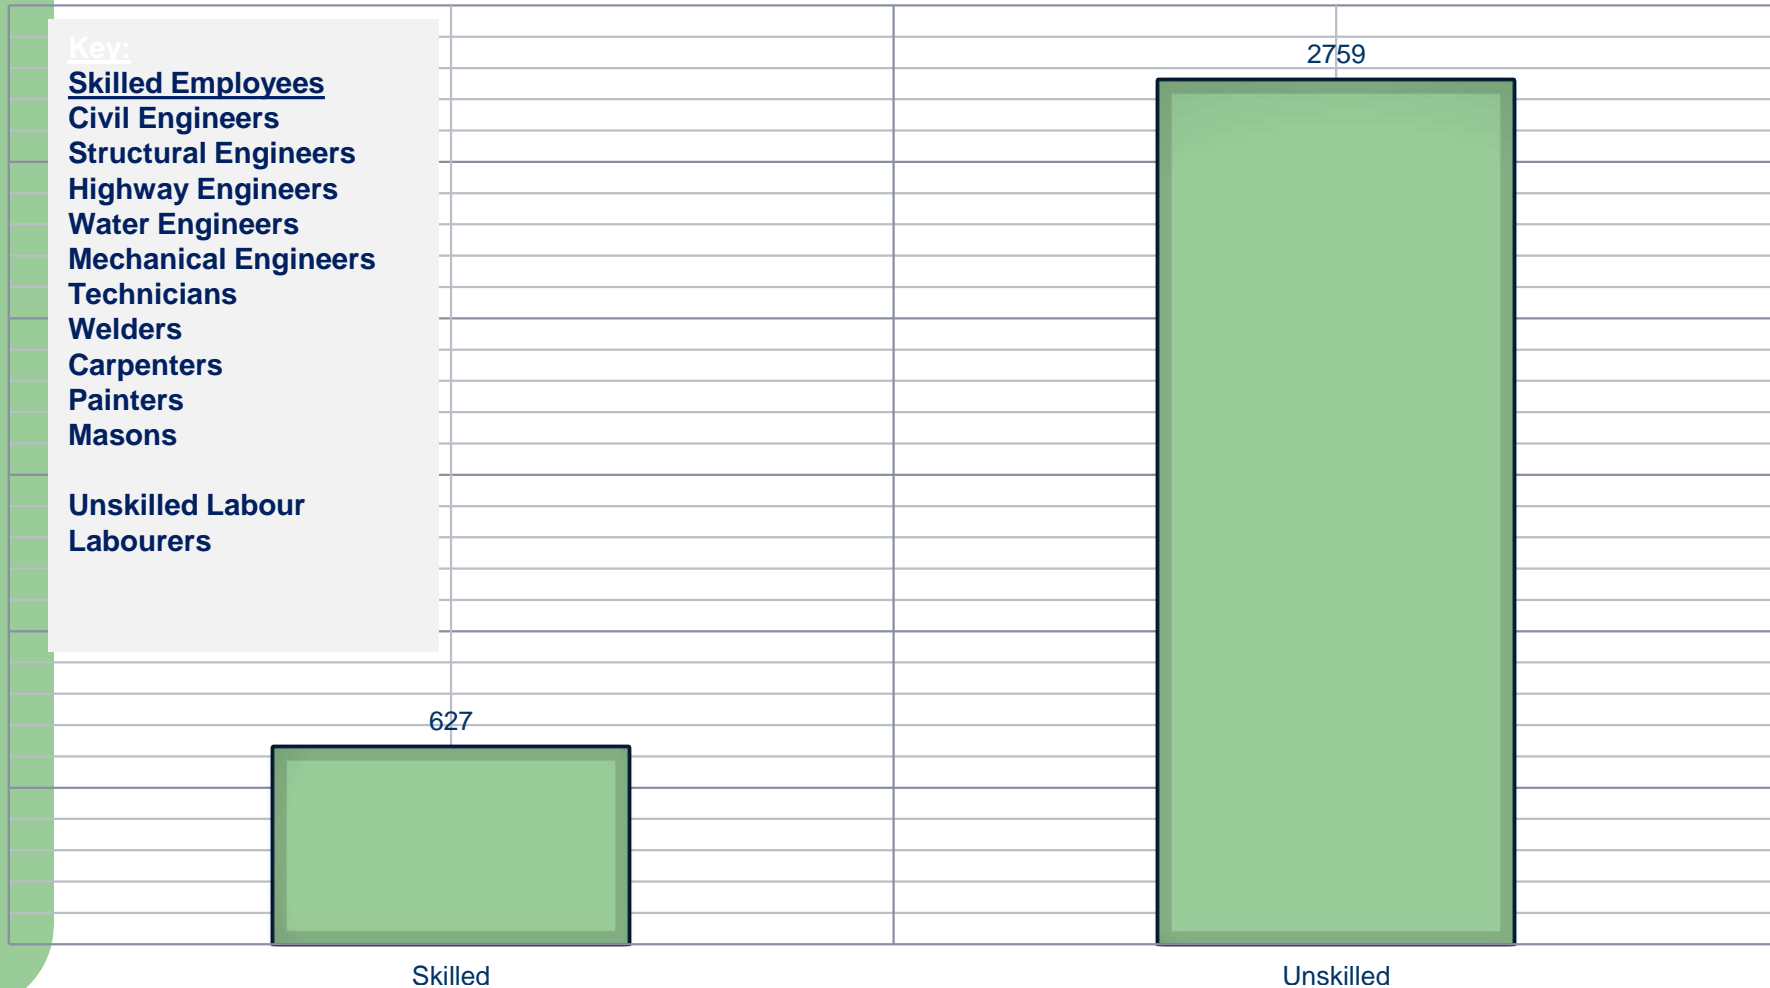

2.2

CABINET AFFAIRS OFFICE

PROGRESS REPORT ON THE IMPLEMENTATION OF THE DECISIONS OF THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM THE CABINET AFFAIRS OFFICE (CAO)

S/N	MEETING OF FEC AND DATE	REFERENCE NUMBER AND SUBJECT OF MEMORANDUM	IMPLEMENTING MDAS	DECISION TAKEN IN COUNCIL	DETAILS OF ACTION TAKEN
1.	EC(2015)14 TH MEETING OF 7 DECEMBER, 2015	AOB: Residential Accommodation for Ministers	CAO	<u>Conclusion 8</u> i. The President directed that proposals be made to address Ministers' accommodation challenge	i. Implemented ii. Report on the Residential Accommodation for Ministers has been approved by the Federal Executive Council and awaiting implementation
2.	EC(2016) 3 RD MEETING OF 17 FEBRUARY, 2016.	1. EC(2016)3: Report of the Cabinet Committee on Nigeria's accession to the (Budapest) Convention on Cybercrime, (CET NO.185).	CAO	<u>Conclusion 4</u> i. Approved the recommendations of the Committee as highlighted in paragraph 9 (i to iii) of the memorandum	i. Cabinet Committee Assignment completed and Report submitted
3	EC(2017)12 TH MEETING OF 29 MARCH , 2017	1. EC(2017)78: Approval for the Report of the Cabinet Committee to Resolve the Issue of Ministerial oversight of the ICT Sector in Nigeria	CAO	<u>Conclusion 5</u> 1. Approved the following recommendations of the Cabinet Committee: Section 148(1) of the Constitution gives the President the power to assign responsibilities and mandates to Ministers and this discretion cannot be constrained by any existing laws,	Cabinet Committee Assignment completed and Report submitted

CABINET AFFAIRS OFFICE

PROGRESS REPORT ON THE IMPLEMENTATION OF THE DECISIONS OF THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM THE CABINET AFFAIRS OFFICE (CAO)

				<p>President to direct the Business of Government should be accepted as the basis of authority for the assignment of mandates to MDAs.</p> <p>The mandates of MDAs are determined by the direction of Government Policy and Extant Laws should be reviewed to support the implementation of Government policy. The Laws regulating the operations of NITDA, NIGCOMSAT Ltd. and Galaxy Backbone Ltd should be reviewed and brought in line with the policy intentions of Government</p> <p>The Policy of Government on the mandates of the Ministries of Science & Technology and Communications is as stipulated in the extant circular conveying the approved responsibilities, structure and parastatals of the two Ministries which is SGF Circular ref. No. 59386/IV/760 of 15 August, 2011. This Circular should be re-issued by this Administration for the avoidance of doubt.</p> <p>The mandate to drive information Technology given to the Ministry of Communications was a deliberate decision of Government to create a specialized sector to leverage the emerging potentials in ICT and this should be kept separate from the MS&T, in accordance with global best practices and the wishes of ICT professional bodies in Nigeria.</p> <p>The Ministry of Communications, which is the rightful agency in which the Presidential Council proposed on e-Government is to be domiciled, should review the composition of the proposed Council and include all critical stakeholders before resubmitting the memorandum to Council.</p>	
--	--	--	--	---	--

CABINET AFFAIRS OFFICE

PROGRESS REPORT ON THE IMPLEMENTATION OF THE DECISIONS OF THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM THE CABINET AFFAIRS OFFICE (CAO)

The Federal MS&T presently has oversight of 17 parastatals, which are mostly research Agencies. It is not optimal for its span of control and effective supervision to further increase the number of parastatals under it and therefore, the *status quo* should be maintained.

There is need for greater collaboration and harmonious working relationship between the Ministries of Communications and Science & Technology to ensure that the end result of innovation is applied to develop the ICT sector.

The full functional review of the mandates of all Ministries should be immediately undertaken and the report presented to the Federal Executive Council for consideration and approval.

Since the Committee did not find any reason to support the objection by the Minister

of Science & Technology that the subjects of the memoranda revolve around the statutory mandates of that Ministry, the Minister of Communications should represent the following two memoranda for Council's consideration.

the Nigeria e-Government Master-Plan 2016-2020.
the Nigeria ICT Sector Roadmap 2016-2019.

CABINET AFFAIRS OFFICE

PROGRESS REPORT ON THE IMPLEMENTATION OF THE DECISIONS OF THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM THE CABINET AFFAIRS OFFICE (CAO)

4	EC(2017)14 TH MEETING OF 12 APRIL, 2017	AOB: Re-activation of the Website of Ministries	CAO	<u>Conclusion 8(ix)</u> i. Directed that every Ministry should submit to Cabinet Affairs Office the upgrade on the status of their official websites, including the names of their appropriate Desk Officers, for presentation to Council.	i. Completed ii. Directory of functional official websites of MDAs already compiled by the Cabinet Affairs Office with the Desk Officers also listed
5	EC(2017)17 TH MEETING OF 10 MAY, 2017	AOB: Need to Adhere to the Rules Guiding the Processing of Council Memoranda	CAO	<u>Conclusion 13(xi)</u> i. Directed that, henceforth, memoranda to be considered at Council meetings must be circulated on or before Friday preceding the meeting	Complied with
6	EC(2017)30 TH MEETING OF 9 AUGUST, 2017	1. EC(2017)186: Approval for the Award of Contract for the Engineering Procurement and Construction of the 3,050mw Mambilla Hydroelectric Power Project, Gembu, Taraba State	CAO	<u>Conclusion 8</u> i. Directed the Cabinet Affairs Office to convey the directive of Council to the AGF/MoJ to enable him propose a suitable date for the meeting with the Minister of Power, Works and Housing within a few days to resolve the likely legal issues that may arise on the matter	Complied with

CABINET AFFAIRS OFFICE

PROGRESS REPORT ON THE IMPLEMENTATION OF THE DECISIONS OF THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM THE CABINET AFFAIRS OFFICE (CAO)

7	EC(2017)33 RD MEETING OF 13 SEPTEMBER, 2017	1. EC(2017)184: Approval for the passage into law of the: Constitution (alteration) Bill, 2017; Electoral Act (Amendment) Bill, 2017; Political Parties and Electoral Offences Commission Bill, 2017; and constituency delimitation centre bill, 2017	CAO	<p><u>Conclusion 5</u></p> <p>i. Stepped down Memorandum EC(2017)184 to enable the Vice President and the Attorney General of the Federation & Minister of Justice to constitute a Cabinet Committee that would examine the Bills, with a view to addressing the issues raised by the Vice president, and submit a Report to Council.</p>	i. Cabinet committee constituted and assignment is on-going
8	EC(2017)35 TH MEETING OF 27 SEPTEMBER, 2017	1. EC(2017)180: Approval of the Draft National Policy on Internally Displaced Persons In Nigeria, 2017	CAO	<p><u>Conclusion 4</u></p> <p>i. Stepped down Memorandum EC(2017)180 on the Draft National Policy on Internally Displaced Persons in Nigeria 2017, for members to further study the policy document and to enable the National Commission for Refugees, Migrants & Internally Displaced Persons to address the issues raised by members and re-present to Council within 2 weeks.</p> <p>i. Directed the Ministry of Interior to put in place mechanisms for effective monitoring of the activities of all organisations assisting the IDPs, and that a Committee should be set up to check the activities of those organisations</p>	i. Cabinet committee constituted and assignment is on-going

CABINET AFFAIRS OFFICE

9.		2. EC(2017)209: Approval for the Report And Recommendations of the Inter-Ministerial Working Committee on the Status of Nigeria's Membership of International Organisations and Associated Financial Obligations	CAO	<p><u>Conclusion 5</u></p> <ul style="list-style-type: none"> i. Stepped down Memorandum EC(2017)209 to enable members to aggregate their views on the Report and re-present same to Council within 2 weeks. i. Directed the Minister of Finance to include all the external statutory obligations in the budget for onward transmission to the National Assembly (NASS) for approval, to avoid the embarrassment which the non-payment of Nigeria's assessed financial obligations to the IOs might cause the country 	i. Cabinet committee constituted and assignment is on-going
10	EC(2017)37 TH MEETING OF 11 OCTOBER, 2017	1. EC(2017)228: Approval of the Report of the Technical Committee on Industrial Relations Matters in the Federal Public Service	CAO	<p><u>Conclusion 4</u></p> <ul style="list-style-type: none"> i. Directed the Acting Secretary to the Government of the Federation to constitute a White Paper Drafting Committee to examine the Report of the Technical Committee on Industrial Relations Matters in the Federal Public Service and submit its recommendations to Council. i. Directed members to critically study the Report and submit their inputs to the Office of the Secretary to the Government of the Federation. i. Directed that the Yayale Ahmed Committee Report be circulated to members for their information and guidance 	<ul style="list-style-type: none"> i. The White Paper Drafting Committee is chaired by Minister of Labour & Employment. i. The assignment is on-going and the Committee would soon report back to Council.

CABINET AFFAIRS OFFICE

PROGRESS REPORT ON THE IMPLEMENTATION OF THE DECISIONS OF THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM THE CABINET AFFAIRS OFFICE (CAO)

11	EC(2017)44 TH MEETING OF 29 NOVEMBER, 2017	AOB: Need to modify the Reporting of Council Discussions Under any Other Business (AOB) in the Conclusions, to Reflect Actionable Decisions/Directives	CAO	<u>Conclusion 9(vii)</u> i. Directed the Council Secretariat to modify its rendition of AOB discussions to capture actionable decisions and directives of Council as appropriate.	i. Complied with ii. Actionable decisions/directives are now reflected under AOB
----	---	--	-----	--	---

2.3

FEDERAL ROAD SAFETY CORPS (FRSC)

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL FROM 2015 TO DATE

S/N	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	REMARKS (PROSPECTS OF COMPLETION)
1	APPROVAL FOR THE AWARD OF CONTRACT FOR THE DIRECT PROCUREMENT OF OPERATIONAL VEHICLES FOR THE FEDERAL ROAD SAFETY CORPS	23/11/2016	FRSC	30 DAYS	100	100	VEHICLES DISTRIBUTED AS ATTACHED

LIST OF FEDERAL ROAD SAFETY CORPS VEHICLES ACQUIRED IN DECEMBER 2016

S/N	MAKE/TYPE	NEW REG NO	COMMAND	CHASSIS NO	DATE OF PURCHASE/ ALLOCATION	CONDITION	PURPOSE
1	IVM P/UP	A01 459 RS	RSHQ TSD	FKZSR31B2ET110079	DEC 2016	FUNCTIONAL	PATROL
2	IVM P/UP	A01 542 RS	RS 5.14 IGARA UNIT	FKZSR31B2ET030051	DEC 2016	FUNCTIONAL	PATROL
3	IVM P/UP	A01 79 RS	RS 6.2 A ODUKPANI OUTPOST	FKZSR31B2ET110039	DEC 2016	FUNCTIONAL	PATROL
4	IVM P/UP	A01 842 RS	RS 8.36 OGORIMAGONGO UNIT	FKZSR31B2ET030160	DEC 2016	FUNCTIONAL	PATROL
5	IVM P/UP	A01 868 RS	RS 4.14 BUKURU UNIT	FKZSR31B2ET110021	DEC 2016	FUNCTIONAL	PATROL
6	IVM P/UP	A01 869 RS	RS 7.18 YANGOJI UNIT	FKZSR31B2ET030022	DEC 2016	FUNCTIONAL	PATROL
7	IVM P/UP	A01 870 RS	RS 5.12 BENIN TOLL GATE UNIT	FKZSR31B2ET110128	DEC 2016	FUNCTIONAL	PATROL
8	IVM P/UP	A01 887 RS	RS 10.31 TALATA MAFARA UNIT	FKZSR31B2ET110093	DEC 2016	FUNCTIONAL	PATROL
9	IVM P/UP	A01 919 RS	RS 8.37 OKENE UNIT	FKZSR31B2ET030021	DEC 2016	FUNCTIONAL	PATROL
10	IVM P/UP	A01 920 RS	RS 2.28 A ILARO OUTPOST	FKZSR31B2ET030091	DEC 2016	FUNCTIONAL	PATROL
11	IVM P/UP	A01 921 RS	RS 2.23 A IBAFO OUTPOST	FKZSR31B2ET110092	DEC 2016	FUNCTIONAL	PATROL
12	IVM P/UP	A01 922 RS	RS 2.23 MOWE UNIT	FKZSR31B2ET030095	DEC 2016	FUNCTIONAL	PATROL
13	IVM P/UP	A01 923 RS	RS 7.111 B BWARI OUTPOST	FKZSR31B2ET030132	DEC 2016	FUNCTIONAL	PATROL
14	IVM P/UP	A01 924 RS	RS 6.13 ISIOKPO UNIT	FKZSR31B2ET110013	DEC 2016	FUNCTIONAL	PATROL
15	IVM P/UP	A01 925 RS	RS 12.21 BIU UNIT	FKZSR31B2ET110057	DEC 2016	FUNCTIONAL	PATROL
16	IVM P/UP	A01 926 RS	RS 7.11 GWAGWALADA UNIT	FKZSR31B2ET110118	DEC 2016	FUNCTIONAL	PATROL
17	IVM P/UP	A01 927 RS	RS 5.21 WARRI UNIT	FKZSR31B2ET110085	DEC 2016	FUNCTIONAL	PATROL
18	IVM P/UP	A01 928 RS	RSHQ TSD	FKZSR31B2ET030172	DEC 2016	FUNCTIONAL	PATROL

LIST OF FEDERAL ROAD SAFETY CORPS VEHICLES ACQUIRED IN DECEMBER 2016

19	IVM P/UP	A01 929 RS	RS 7.26 SABON WUSE UNIT	FKZSR31B2ET030066	DEC 2016	FUNCTIONAL	PATROL
20	IVM P/UP	A01 930 RS	RS 2.114 WHARF UNIT	FKZSR31B2ET110162	DEC 2016	FUNCTIONAL	PATROL
21	IVM P/UP	A01 931 RS	RS 11.37 KISI UNIT	FKZSR31B2ET110129	DEC 2016	FUNCTIONAL	PATROL
22	IVM P/UP	A01 932 RS	RS 7.1 FCT SECTOR	FKZSR31B2ET030127	DEC 2016	FUNCTIONAL	PATROL
23	IVM P/UP	A01 933 RS	RS 7.12 ABAJI UNIT	FKZSR31B2ET030116	DEC 2016	FUNCTIONAL	PATROL
24	IVM P/UP	A01 934 RS	RS 8.34 ZARIAGI	FKZSR31B2ET110105	DEC 2016	FUNCTIONAL	PATROL
25	IVM P/UP	A01 935 RS	RS 9.32 KM 78 ABA UNIT	FKZSR31B2ET110005	DEC 2016	FUNCTIONAL	PATROL
26	IVM P/UP	A01 936 RS	RS 9.23 NKALAGU	FKZSR31B2ET110043	DEC 2016	FUNCTIONAL	PATROL
27	IVM P/UP	A01 937 RS	RS 5.16 UWAN-ESIGIE UNIT	FKZSR31B2ET030019	DEC 2016	FUNCTIONAL	PATROL
28	IVM P/UP	A01 938 RS	RS 6.4 BAYELSA SECTOR	FKZSR31B2ET110178	DEC 2016	FUNCTIONAL	PATROL
29	IVM P/UP	A01 939 RS	RS 11.33 APATA UNIT	FKZSR31B2ET110112	DEC 2016	FUNCTIONAL	PATROL
30	IVM P/UP	A01 950 RS	RS 7.26 A TAFA OUTPOST	FKZSR31B2ET110031	DEC 2016	FUNCTIONAL	PATROL
31	IVM P/UP	A01 951 RS	RS 8.12 A ODO-OWA OUTPOST	FKZSR31B2ET110025	DEC 2016	FUNCTIONAL	PATROL
32	IVM P/UP	A01 952 RS	RS 8.1 A IDOFIAN OUTPOST	FKZSR31B2ET110154	DEC 2016	FUNCTIONAL	PATROL
33	IVM P/UP	A01 953 RS	RS 2.21A GATE 3 OUTPOST IJEBU-ODE	FKZSR31B2ET030060	DEC 2016	FUNCTIONAL	PATROL
34	IVM P/UP	A01 954 RS	RS 1.42 GUMEL UNIT	FKZSR31B2ET110158	DEC 2016	FUNCTIONAL	PATROL
35	IVM P/UP	A01 955 RS	RSHQ TSD COBRA	FKZSR31B2ET030118	DEC 2016	FUNCTIONAL	PATROL
36	IVM P/UP	A01 956 RS	RS 11.21 A AJEBANDELE OUTPOST	FKZSR31B2ET030143	DEC 2016	FUNCTIONAL	PATROL
37	IVM P/UP	A01 957 RS	RS 11.14 IKIRUN	FKZSR31B2ET110003	DEC 2016	FUNCTIONAL	PATROL
38	IVM P/UP	A01 958 RS	RS 10.2A YAURI OUTPOST	FKZSR31B2ET110026	DEC 2016	FUNCTIONAL	PATROL
39	IVM P/UP	A01 959 RS	RS 11.16 GBONGAN UNIT	FKZSR31B2ET110161	DEC 2016	FUNCTIONAL	PATROL
40	IVM P/UP	A01 960 RS	RS 11.24 ASEJERE UNIT	FKZSR31B2ET110087	DEC 2016	FUNCTIONAL	PATROL

LIST OF FEDERAL ROAD SAFETY CORPS VEHICLES ACQUIRED IN DECEMBER 2016

1	PGT 301 ACCESS	06-04 RS	RSHQ MVA (HEAD PLANT GWA/LADA)	VF3DDHMYBDJ847434	DEC 2016	FUNCTIONAL	ADMIN
2	PGT 301 ACCESS	24-04 RS	RS 2.0 LAGOS ZONAL COMMAND	VF3DDHMYBEJ699925	DEC 2016	FUNCTIONAL	ADMIN
3	PGT 301 ACCESS	32-04 RS	RS 10.2 KEBBI SECTOR	VF3DDHMYBDJ877755	DEC 2016	FUNCTIONAL	ADMIN
4	PGT 301 ACCESS	37-04 RS	RS 12.3 YOBE SECTOR	VF3DDHMYBFJ546682	DEC 2016	FUNCTIONAL	ADMIN
5	PGT 301 ACCESS	52-04 RS	RSHQ MVA (HOS PRINT FARM)	VF3DDHMYBEJ549807	DEC 2016	FUNCTIONAL	ADMIN
6	PGT 301 ACCESS	55-04 RS	RS 4.3 NASARAWA SECTOR COMDR	VF3DDHMYBFJ546669	DEC 2016	FUNCTIONAL	ADMIN
7	PGT 301 ACCESS	57-04 RS	RS 12.2 BORNO SECTOR	VF3DDHMYBDJ877759	DEC 2016	FUNCTIONAL	ADMIN
8	PGT 301 ACCESS	59-04 RS	RS 10.1 SOKOTO SECTOR CMDR	VF3DDHMYBEJ546155	DEC 2016	FUNCTIONAL	ADMIN
9	PGT 301 ACCESS	60-04 RS	RS 12.1 BAUCHI SECTOR	VF3DDHMYBDJ877762	DEC 2016	FUNCTIONAL	PATROL
10	PGT 301 ACCESS	61-04 RS	RS 11.1 OSUN SECTOR	VF3DDHMYBDJ819994	DEC 2016	FUNCTIONAL	ADMIN
11	PGT 301 ACCESS	64-04 RS	RSHQ TRG CMDT JOS	VF3DDHMYBDJ887148	DEC 2016	FUNCTIONAL	ADMIN
12	PGT 301 ACCESS	65-04 RS	RS 10.3 ZAMFARA SECTOR CMDR	VF3DDHMYBDJ877761	DEC 2016	FUNCTIONAL	ADMIN
13	PGT 301 ACCESS	72-04 RS	RS 9.3 ABIA SECTOR	VF3DDHMYBDJ887149	DEC 2016	FUNCTIONAL	ADMIN
14	PGT 301 ACCESS	73-04 RS	RS 8.2 EKITI SECTOR	VF3DDHMYBFJ546657	DEC 2016	FUNCTIONAL	ADMIN
15	PGT 301 ACCESS	85-04 RS	RS 7.1 FCT SECTOR	VF3DDHMYBFJ533271	DEC 2016	FUNCTIONAL	ADMIN
16	PGT 301 ACCESS	93-04 RS	RS 5.3 HEAD AWKA PLANT	VF3DDHMYBDJ805296	DEC 2016	FUNCTIONAL	ADMIN
17	PGT 301 ACCESS	98-04 RS.	RS 8.3 KOGI SECTOR	VF3DDHMYBFJ539979	DEC 2016	FUNCTIONAL	ADMIN
18	PGT 301 ACCESS	99-04 RS	RSHQ PIO	VF3DDHMYBFJ546684	DEC 2016	FUNCTIONAL	ADMIN
19	PGT 301 ACCESS	A01 940 RS	RS 7.111 A GWARIMPA OUT POST	VF3DDHMYBFJ546663	DEC 2016	FUNCTIONAL	PATROL
20	PGT 301 ACCESS	A01 941 RS	RS 11.13 IPETU-IJESHA	VF3DDHMYBDJ881229	DEC 2016	FUNCTIONAL	PATROL
21	PGT 301 ACCESS	A01 943 RS	RS 11.35 EGBEDA UNIT	VF3DDHMYBDJ881230	DEC 2016	FUNCTIONAL	PATROL
22	PGT 301 ACCESS	A01 945 RS	RS 7.11 GWAGWALADA UNIT	VF3DDHMYBFJ546674	DEC 2016	FUNCTIONAL	PATROL
23	PGT 301 ACCESS	A01 946 RS	RSHQ TSD	VF3DDHMYBDJ864528	DEC 2016	FUNCTIONAL	ADMIN
24	PGT 301 ACCESS	A01 947 RS	RS 7.110 LUGBE UNIT	VF3DDHMYBDJ805295	DEC 2016	FUNCTIONAL	PATROL
25	PGT 301 ACCESS	A01 948 RS	RS 11.12 ILESHA	VF3DDHMYBDJ873928	DEC 2016	FUNCTIONAL	PATROL
26	PGT 301 ACCESS	A01 949 RS	RS 7.1 A MPAPE OUTPOST	VF3DDHMYBFJ546675	DEC 2016	FUNCTIONAL	PATROL
27	PGT 301 ACCESS	HQ 96 RS	RSHQ TSD	VF3DDHMYBFJ546696	DEC 2016	FUNCTIONAL	ADMIN

SUMMARY:

IVM PICK -UP = 40

PGT 301 ACCESS = 27

2.4

NATIONAL HAJJ COMMISSION OF NIGERIA (NAHCON)

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE
FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

S/NO	PROJECT TITLE	COST OF PROJECT (N)	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSD BY THE PROJECT	STATUS OF IMPLEMENT ATION (%)	REMARKS (PROSPECT OF COMPLETION)
1.	Acquisition, and Renovation of Acquired Properties, Furnishing and Equipping the Properties, and Relocation of Office to the newly Acquired Properties named Metrol Plaza, at Plot 991/992 Mailari Street, Central Business District, FCT, Abuja.	.	8 TH NOVEMBER, 2017.	National Hajj Commission of Nigeria (HAHCON)	2017 - 2019	<ul style="list-style-type: none"> ▪ Partly funded from Savings from Service Charges to Pilgrims and Capital Budget Appropriation Act of 2017. ▪ The sum of N1.5B was raised from Hajj Savings over the past years; ▪ Balance was to be funded from Year 2017 Budget Appropriation out of which 50% had been released. 	75% Completion (Properties purchased. Un-renovated)	<ul style="list-style-type: none"> ▪ Awaiting the Balance to be returned to Hajj Account. ▪ The Funds required for renovation and Furnishing of the new Office has been included in the 2018 Budget Proposal

2.5

NATIONAL PENSION COMMISSION

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL FROM MAY 2015 TO DECEMBER 2017

S/N	PROJECT TITLE	COST OF PROJECT	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	REMARKS (PROSPECTS OF COMPLETION)
1	Direct Procurement and Acquisition of Microsoft Office 365 Enterprise License	\$539,130.72@N304.75/\$ = ₦164,300,086.92 to be paid in 3 no equal instalment over a period of 3 years	11/1/2017 (approved by Federal Executive Council)	National Pension Commission	Within five (5) working days from the execution of contract agreement. A license is given	33.33% (₦ 54,766,695.64)	70% (Deployment of Licenses)	Deployment of Licenses as at February 2018: <ol style="list-style-type: none"> 1. Microsoft Office Plus Professional 2016 (400 Licenses) 2. SharePoint Server Enterprise 2016 (1 Server) 3. Project Professional 2013 (5 Licenses) 4. Windows Server 2016 (5 Licenses) 5. SQL Server Standard Core 2017 (1 Server) 6. Windows 10

2.6


NATIONAL POPULATION COMMISSION THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

S/ N	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	REMARKS (PROSPECTS OF COMPLETION)
1	Direct Procurement of Five Toyota Land Cruiser Jeeps; One Toyota Hilux Double Cabin Pick-Up One Toyota Coaster Bus for Operational uses.	17/05/2017	National Population Commission	30 Days	N308,480,000.00	100%	Completed

2.7

ECONOMIC AND FINANCIAL CRIMES COMMISSION THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE FEDERAL EXECUTIVE COUNCIL (FEC) FROM MAY 2015 TO DECEMBER 2017

S/N	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	REMARKS (PROSPECTS OF COMPLETION)
1	Award of Contracts for the Direct Procurement of Operational Vehicles for the Economic and Financial Crimes Commission (EFCC)	12/10/2016	EFCC		100%	Completed	
2	Award of Contract for revised estimated total cost for the Contract for the Completion of the On-going Construction of the EFCC Corporate Headquarters Office, Abuja	26/4/2017	EFCC		80%	On-going	
3	Award of Contract for the Provision of Internet Broadband and Firewall for the EFCC Headquarters and all its Zonal Offices	6/12/2017	EFCC	8 Weeks	0%	On-going	



**PICTORIAL EVIDENCES OF SOME OF
THE APPROVED FEDERAL EXECUTIVE
COUNCIL (FEC) PROJECTS FROM
MAY 2015 TO DECEMBER 2017**

ECOLOGICAL FUND OFFICE

UNIVERSITY OF CALABAR EROSION & FLOOD CONTROL WORKS, CALABAR, CROSS RIVER STATE



BEFORE



Above represents sample of parts of the ecological site before the commencement of work

UNIVERSITY OF CALABAR EROSION & FLOOD CONTROL WORKS, CALABAR, CROSS RIVER STATE

DURING



Above represents sample of parts of the on-going work at site

UNIVERSITY OF CALABAR EROSION & FLOOD CONTROL WORKS, CALABAR, CROSS RIVER STATE



Above represents sample of parts of completed work

REMEDIATION OF THE HYDROCARBON SLUDGE AT THE WARRI REFINERY AND PETROCHEMICAL COMPANY PHASE II, WARRI SOUTH LGA, DELTA STATE.



Above represents sample of parts of the ecological sites before the commencement of work



Above represents sample of parts of the on-going work at the site




Above represents sample of parts of the completed work

EROSION CONTROL IN AWLAW TOWN, OJI RIVER L.G.A. ENUGU STATE



EROSION CONTROL IN AWLAW TOWN, OJI RIVER L.G.A. ENUGU STATE

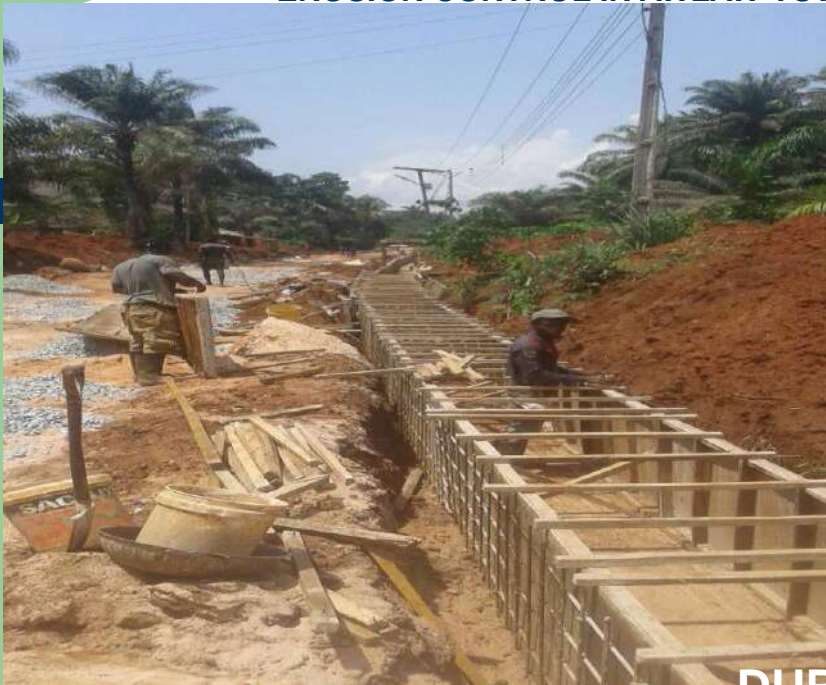

DURING



Above represents sample of parts of the on-going work at the site

EROSION CONTROL IN AWLAW TOWN, OJI RIVER L.G.A. ENUGU STATE



CHANNELISATION AND DE-SILTING OF OKOKO AND OGBAGBA RIVERS IN OSOGBO, OSUN STATE

BEFORE



Above represents sample of parts of the ecological sites before commencement of work

DURING



Above represents sample of parts of the on-going work at the site

AFTER



Above represents sample of parts of the completed work

RIJAU, DUGGE, DUKKU, T/MAGAJIYA AND GENU EROSION AND FLOOD CONTROL, RIJAU LGA, NIGER STATE



Above represents sample of parts of the ecological site before the commencement of work



RIJAU, DUGGE, DUKKU, T/MAGAJIYA AND GENU EROSION AND FLOOD CONTROL, RIJAU LGA, NIGER STATE



Malam Tsoho road Dukku




AFTER

DIRRI / AWALA ROAD RIJAU



RATAYAGIWA RIJAU

1 / 12/2017

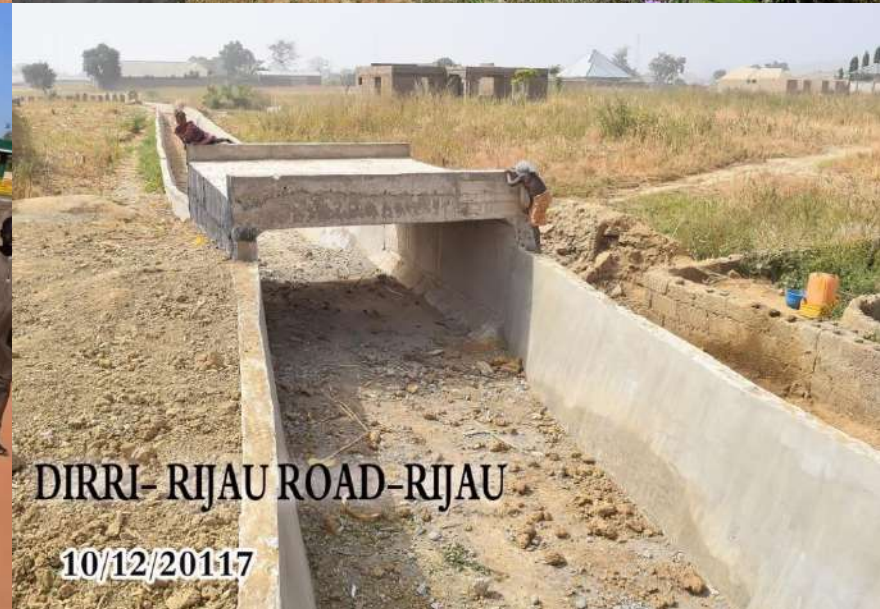

DIRRI- RIJAU ROAD-RIJAU

10/12/20117

Above represents sample of parts of the completed work



Above represents sample of parts of the on-going work at the site

DAURA TOWNSHIP EROSION CONTROL, PHASE I, DAURA, KATSINA STATE

AFTER



Above represents sample of parts of the completed work

COMMISSIONED AND HANDED OVER



Above represents sample of parts of the completed work

KWOI EROSION AND FLOOD CONTROL WORKS, JABA, KADUNA STATE



BEFORE



KWOI EROSION AND FLOOD CONTROL WORKS, JABA, KADUNA STATE



KWOI EROSION AND FLOOD CONTROL WORKS, JABA, KADUNA STATE



SABKE/DUTSI AND MASHI WATER SUPPLY PROJECT, KATSINA STATE AWAITING COMMISSIONING



Above represents sample of parts of the on-going work at the site

EROSION CONTROL WORKS AT ALEX EKWUEME UNIVERSITY, NDUFU ALIKE IKWO, EBONYI STATE

BEFORE



Above represents sample of parts of the ecological site before the commencement of work

EROSION CONTROL WORKS AT ALEX EKWUEME UNIVERSITY, NDUFU ALIKE IKWO, EBONYI STATE

DURING



27 03 2017



Above represents sample of parts of the on-going work at the site

EROSION CONTROL WORKS AT ALEX EKWUEME UNIVERSITY, NDUFU ALIKE IKWO, EBONYI STATE



Above represents sample of parts of the completed work


EROSION CONTROL WORKS AT ODO ALAAMO, OGBOMOSO, OYO STATE



Above represents sample of parts of the ecological site before the commencement of work



Above represents sample of parts of the on-going work at the site

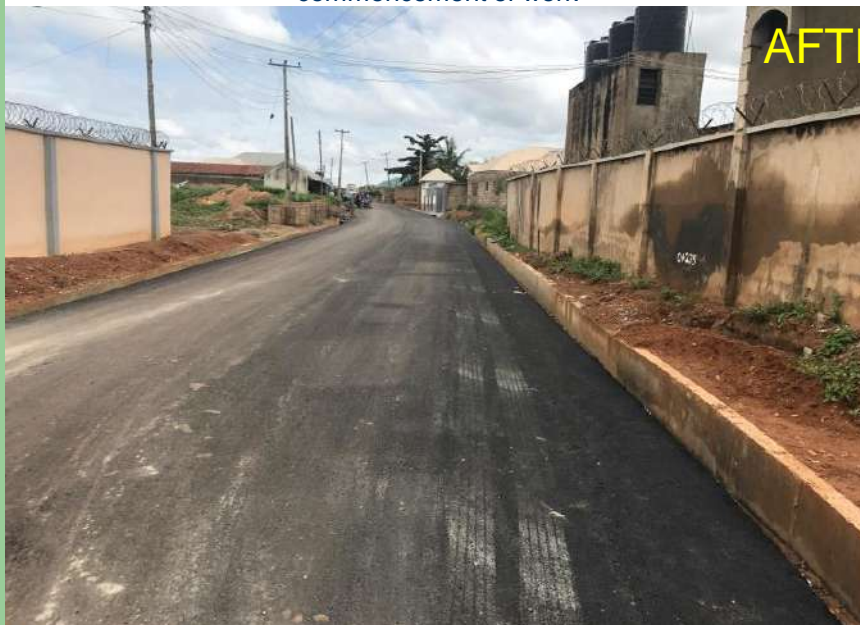

Above represents sample of parts of the completed work



FLOOD AND EROSION CONTROL WORKS , DAMATURU – BALMARI – GASHUA ROAD, DAMATURU LGA, YOBE STATE



BEFORE



Above represents sample of parts of the ecological site before the commencement of work

FLOOD AND EROSION CONTROL WORKS , DAMATURU – BALMARI – GASHUA ROAD, DAMATURU LGA, YOBE STATE



DURING



Above represents sample of parts of the on-going work at the site



Above represents sample of parts of the on-going work at the site

GULLY EROSION CONTROL WORKS AT VERITAS UNIVERSITY, BWARI, ABUJA

BEFORE



Above represents sample of parts of the ecological site before the commencement of work

DURING



Above represents sample of parts of the on-going work at the site

AFTER



Above represents sample of parts of the completed work



EROSION AND FLOOD CONTROL WORKS AT PROJECT DEVELOPMENT INSTITUTE (PRODA), FEDERAL MINISTRY OF SCIENCE & TECHNOLOGY ENUGU STATE



EROSION AND FLOOD CONTROL WORKS AT PROJECT DEVELOPMENT INSTITUTE (PRODA), FEDERAL MINISTRY OF SCIENCE & TECHNOLOGY ENUGU STATE



Above represents sample of parts of the on-going work at the site

DISILTING OF OGBAGBA AND OKOKO RIVERS, OSHOGBO, PHASE I & II, OSUN STATE



DISILTING OF OGBAGBA AND OKOKO RIVERS, OSHOGBO, PHASE I & II, OSUN STATE



Above represents sample of parts of the on-going work at the site

SHORELINE PROTECTION, ALEBIRI, BAYELSA STATE



BEFORE



SHORELINE PROTECTION, ALEBIRI, BAYELSA STATE

ON-GOING



Above represents sample of parts of the on-going work at the site

ABAJI GULLY EROSION AND FLOOD CONTROL WORKS ABAJI AREA COUNCIL, ABUJA



ABAJI GULLY EROSION AND FLOOD CONTROL WORKS ABAJI AREA COUNCIL, ABUJA



Above represents sample of parts of the on-going work at the site

ABAJI GULLY EROSION AND FLOOD CONTROL WORKS ABAJI AREA COUNCIL, ABUJA



AZARE TOWNSHIP FLOOD AND EROSION CONTROL WORKS, AZARE, BAUCHI STATE

BEFORE



AZARE TOWNSHIP FLOOD AND EROSION CONTROL WORKS, AZARE, BAUCHI STATE



Above represents sample of parts of the on-going work at the site

AZARE TOWNSHIP FLOOD AND EROSION CONTROL WORKS, AZARE, BAUCHI STATE



CHANNELIZATION AND FLOOD CONTROL OF PONJ-AFO RIVER, IKIRUN, OSUN STATE: PICTORIALS OF SITE BEFORE COMMENCEMENT OF WORK



CHANNELIZATION AND FLOOD CONTROL OF PONJ-AFO RIVER, IKIRUN, OSUN STATE:



Above represents sample of parts of the on-going work at the site

CHANNELIZATION AND FLOOD CONTROL OF PONJ-AFO RIVER, IKIRUN, OSUN STATE:



EROSION AND FLOOD CONTROL WORKS AT IFEDAYO/BOLUWADURO/ILA, OSUN STATE



Above represents sample of parts of the ecological site before the commencement of work

EROSION AND FLOOD CONTROL WORKS AT IFEDAYO/BOLUWADURO/ILA, OSUN STATE



Above represents sample of parts of the on-going work at the site

EROSION AND FLOOD CONTROL WORKS AT IFEDAYO/BOLUWADURO/ILA, OSUN STATE





Above represents sample of parts of the acquired vehicles



Above represents sample of parts of the acquired vehicles

NATIONAL HAJJ COMMISSION OF NIGERIA (NAHCON) ACQUIRED PROPERTY



NATIONAL PENSION COMMISSION (Volume License Agreement)



Volume Licensing

Program Signature Form

MBA/MBSA number

U7234458

7-KSHPWICM3

Agreement number

35E66157

Note: Enter the applicable active numbers associated with the documents below. Microsoft requires the associated active number be indicated here, or listed below as new.

For the purposes of this form, "Customer" can mean the signing entity, Enrolled Affiliate, Government Partner, Institution, or other party entering into a volume licensing program agreement.

This signature form and all contract documents identified in the table below are entered into between the Customer and the Microsoft Affiliate signing, as of the effective date identified below.

Contract Document	Number or Code
Microsoft Business and Services Agreement	X20-10006
Enterprise Agreement	X20-10094
<Choose Agreement>	Document Number or Code
<Choose Agreement>	Document Number or Code
<Choose Agreement>	Document Number or Code
Enterprise Enrollment	X20-10379
<Choose Enrollment/Registration>	Document Number or Code
<Choose Enrollment/Registration>	Document Number or Code
<Choose Enrollment/Registration>	Document Number or Code
<Choose Enrollment/Registration>	Document Number or Code
Enterprise Amendment	M19-7-KSHPWICM3
Enterprise Agreement Customer Price Sheet	0563018.008
Product Selection Form	PSF-0563018.008

By signing below, Customer and the Microsoft Affiliate agree that both parties (1) have received, read and understand the above contract documents, including any websites or documents incorporated by reference and any amendments and (2) agree to be bound by the terms of all such documents.

Customer

Name of Entity (must be legal entity name)* National Pension Commission

Signature*

Printed First and Last Name* CHINELO ANOHU-AMAZU

Printed Title DIRECTOR - GENERAL

Signature Date* 30 MARCH, 2017

* indicates required field

Microsoft Affiliate
Microsoft Ireland Operations Limited
VAT number IE8256796U
Signature _____
Printed First and Last Name _____
Printed Title _____
Signature Date (date Microsoft Affiliate countersigns)
Agreement Effective Date (may be different than Microsoft's signature date)
30.03.2017

Optional 2nd Customer signature or Outsourcer signature (if applicable)

Customer
Name of Entity (must be legal entity name)* NATIONAL PENSION COMMISSION
Signature* <i>[Signature]</i>
Printed First and Last Name* MUHAMMAD CANI MUHAMMAD
Printed Title COMMISSION SECRETARY/LEGAL ADVISER
Signature Date* 27 MARCH, 2017

* indicates required field

Outsourcer
Name of Entity (must be legal entity name)*
Signature* _____
Printed First and Last Name* _____
Printed Title _____
Signature Date* _____

* indicates required field

If Customer requires physical media, additional contacts, or is reporting multiple previous Enrollments, include the appropriate form(s) with this signature form.

After this signature form is signed by the Customer, send it and the Contract Documents to Customer's channel partner or Microsoft account manager, who must submit them to the following address. When the signature form is fully executed by Microsoft, Customer will receive a confirmation copy.

Microsoft Ireland Operations Limited

Atrium Building Block B
Carmenhall Road
Sandyford Industrial Estate
Dublin 18, Ireland
Attention: EOC Program Operations Dept.

I certify this is a true and correct copy of this document effective 31 MAR 2017 24 APR 2017 <i>[Signature]</i> Microsoft Microsoft Ireland Operations Ltd. Damien Martini Duly Authorized on behalf of Commercial Customer Operations
--

NATIONAL POPULATION COMMISSION PURCHASED VEHICLES



NATIONAL POPULATION COMMISSION PURCHASED VEHICLES



ECONOMIC AND FINANCIAL CRIMES COMMISSION (EFCC) PURCHASED OPERATIONAL VEHICLES



Above represents sample of parts of the purchased Operational Vehicles

CONSTRUCTION OF THE ECONOMIC AND FINANCIAL CRIMES COMMISSION (EFCC)'S CORPORATE HEADQUARTERS




Above represents sample of parts of the on-going construction work at the site



**TABLE OF COMPLETED ECOLOGICAL
FUND PROJECTS FROM
MAY 2015 TO DECEMBER 2017
READY FOR COMMISSIONING:
DETAILS ARE SHOWN IN ANNEX (II)**



THANK YOU



ANNEX (I)

**ECOLOGICAL FUND OFFICE (EFO) PROJECTS
BELOW FEDERAL EXECUTIVE COUNCIL (FEC)
THRESHHOLD FROM MAY 2015 TO DECEMBER 2017**

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
1	Provision of Public Conveniences in (3) LGAs, Ibadan, Oyo State: i. Mogaji Market, Iyana Agbala along New Ibadan-Ife Road, Egbeda LGA; ii. Jonku Neighbourhood Market along Iwo Road Interchange, Ojo Expressway, Ibadan North East LGA; and iii. Orita Aperin Market, Orita Aperin Ibadan South LGA.	July, 2015.	Ecological Fund Office	3 Months	N/A	100%	18	The Scope of work include: i. Site Clearance; ii. Excavation of Pit; iii. Backfill and removal of excess of soil; iv. Construction of Conveniences; v. Drilling of Boreholes sealed with overhead Steel Tank and Solar Panels. The project is 100% completed. Commissioned and handed over.
2	Soil Erosion Control Works at Usho/Ise Road, Ondo State.	November, 2015.	Ecological Fund Office	1 Month.	N/A	100%	30	The Scope of work include: Site clearing / earth works and Construction of Culverts and Drainages. The project is 100% completed and awaiting commissioning and handing over.
3	Soil Erosion Control Works At Zuba	November, 2015.	Ecological Fund Office	1 Month.	N/A	100%	25	The Scope of work include: i. Site Clearance; ii. Earthworks and Excavation; iii. Construction of Reinforced Concrete Lined Channels; iv. Construction of Concrete Culverts. The project is 100% completed. Commissioned and handed over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
4	Doma Flood Erosion Control Works, Nasarawa State	November, 2015.	Ecological Fund Office	4 Months	N/A	100%	25	The Scope of work include: Construction of drainage channels; Demolition & removal of existing blocked/weak/inadequate stream crossing structures and drainages; Connection of existing Channels to the newly constructed Channels; Stone-Pitching and Rock dump for erosion control works; and Construction of Access Culverts and provision of access Slabs across the drainage Channels. The project is 100% completed and handed over
5	Lohmak-Kumkwum Erosion Control Works, Langtang North LGA, Plateau State	November, 2015.	Ecological Fund Office	4 Months	N/A	100%	25	The Scope of work include: Site clearing and Earth works; Reinforcement of concrete and lined channels; and Reinforcement of box culverts. The Project is 100% completed and handed over.
6	Gully Erosion Control Works at Magodo, Lagos State	December, 2015.	Ecological Fund Office	6 Month.	N/A	100%	28	The Scope of work include: i. Site Clearance; ii. Earthworks and Excavation; iii. Construction of concrete drains/channels; iv. Stone Pitching; and v. Construction of concrete retaining wall. The project is 100% completed. Commissioned and handed over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
7	Oghere Ahmed Erosion Control Works, Idimu, Lagos	December, 2015.	Ecological Fund Office	6 Months.	N/A	100%	25	The Scope of work include: i. Site Clearance; ii. Earthworks and Excavation; iii. Construction of Reinforced Concrete Lined Channels; iv. Construction of Concrete Culverts. The project is 100% completed. Commissioned and handed over.
8	Kudeti Flood Control Works, Ibadan Oyo State	December, 2015.	Ecological Fund Office	5 Months.	N/A	100%	28	The Scope of work include: i. Site Clearance; ii. Demolition and removal of existing blocked/weak and inadequate structures; iii. Construction of reinforced rectangular and trapezoidal drains/channels; iv. Construction of culverts and access slabs; and v. Stone Pitching. The project is 100% completed. Commissioned and handed over.
9	Umudiato Flood Control Works, Orlu LGA, Imo State	February 4th, 2016	Ecological Fund Office	4 Months	N/A	100%	25	Scope of work include: Construction of one side trapezoidal concrete drains; Construction of appropriately sized box culverts; and Road improvement works. The project is '100% completed and awaiting commissioning.

**THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS
BOARD FROM MAY 2015 TO DECEMBER 2017**

SN	PROJECT TITLE	COST OF PROJECT (N)	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
10	Umuoki-Umuowasi Erosion Control and Road Improvement Works.	200,382,392.19	March, 2016	Ecological Fund Office	4 Months	N/A	100%	28	Scope of work include: Construction of 2.4km drains; Provision of concrete drains and culverts; and Road improvement works. The project is 100% completed. Commissioned and handed over.
11	Owalla Avuvu Erosion Control Works, Imo State	N176,504,612.81	March, 2016	Ecological Fund Office	5 Months.	N/A	100%	25	Scope of work include: Earth works; Concrete Drains/Culverts; Box Culverts and Stone-pitching. The project is 100% completed and handed over.
12	Model Village Development, Adamawa and Gombe States.	N168,147,104.52	July, 2016.	Ecological Fund Office	10 Months	N/A	100%	25	The Scope of work include: i. Construction of Solar Powered Borehole; ii. 5000 Liters Overhead Water Supply Tank; iii. 50 Seating Capacity Community Viewing Centre. The project is 100% completed. Awaiting commissioning and handing over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
13	Reconstruction of Maska Earth Dam, Maska Funtua, Katsina State	November, 2016	Ecological Fund Office	3 Months	N/A	100%	28	Scope of work include: Construction of earth Dam; Construction of Spillway, Embankment and Surface dressed road. The project is 100% completed and handed over
14	Contract for Erosion and Flood control Work in Bogoro LGA Bauchi State	March 6th, 2017.	Ecological Fund Office	6 Months	N/A	100%	28	Scope of work include the following: i. Construction of 2 No. Culverts length 18m, ii. Construction of Walkway Access Road of 700m. Project is 100% Completed. Awaiting commissioning and handing over.
15	Soil Erosion Control Works at Nigerian Police Housing Estate Kurudu, Abuja, FCT.	March, 2017	Ecological Fund Office	4 Months	N/A	100%	28	The Scope of work include: Concrete Retaining wall and earth works. The Contract is 100% completed and handed over

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
16	Gadan Toro to Market Road Erosion Control Works, Toro LGA, Bauchi State.	March, 2017	Ecological Fund Office	9 Months	N/A	100%	28	Scope of work include: Site Clearance and Earth work; Concrete works/Retaining wall; and Rehabilitation of Eroded Road. The project is 100% completed and awaiting commissioning.
17	Erosion/Flood Control Project of Rice Field, Shanga LGA, Kebbi State	March 9th, 2017	Ecological Fund Office	4 Months	N/A	100%	18	Scope of work include: Construction and Rehabilitation of Dam embankment; Expansion of Spillway; Construction of Discharge Channels and flood control Dyke. The project is 100% completed and awaiting commissioning and handing over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
18	Gully Erosion Control Works at Federal Government College, Otobi, Benue State	March, 2017	Ecological Fund Office	4 Months	N/A	100%	25	Scope of work include: Removing of blocked drains/Culverts and Earth works. The project is 100% completed and awaiting Commissioning and Handing Over
19	Channelization and Flood Control of Ponj-Afo River, Ikirin, Osun State	March 4th, 2017	Ecological Fund Office	6 Months	N/A	100%	30	Scope of work include: Site clearing; Construction of Culverts; Carting away of all loosed materials & debris; and asphalt overlay road. The project is 100% completed and awaiting commissioning and handing over.
20	Ganye-Yelwa Road Erosion and Flood Control Works, Ganye LGA, Adamawa State	March 3rd, 2017	Ecological Fund Office	10 Months	N/A	100%	28	Scope of work include: Construction of earth road; Construction of concrete drain 800m long; Construction of 5No. Reinforced concrete Culverts, double cell/single cell; and Stone-Pitching of road/drain side 500m. The project is 100% completed. Awaiting commissioning.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
21	Ganye-Dabora-Daksam Road Erosion and Flood Control Works, Ganye LGA and Reconstruction of Jada Water Works System, Adamawa State	March, 2017	Ecological Fund Office	7 Months	N/A	100%	30	Scope of work include: Construction of concrete drains; Concrete culverts; Earth works; and rehabilitation of water supply. The project is 100% completed and awaiting Commissioning and Handing Over.
22	Azare Township Flood and Erosion Control Works, Bauchi State.	March, 2017	Ecological Fund Office	5 Months	N/A	100%	28	Scope of work include: Site Clearance; Concrete Drains at GDSS Azare; Matsago Low Cost Housing; Old Airport and Cemetery; Culverts and Access Slabs. The project is 100% completed. To be commissioned and handed over.
23	Tsoho Gwaram Erosion and Flood Control Project, Gwaram LGA, Jigawa State	March, 2017	Ecological Fund Office	10 Months	N/A	100%	28	Scope of work include: Site clearance and earth works; Concrete works; Reinforced concrete drainages, culverts and access slabs. The project is 100% completed. Awaiting commissioning and handing over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
24	Kumo Gully Erosion Site, Anguwan Jauro Musa, Akko LGA, Gombe State	March, 2017	Ecological Fund Office	5 Months	N/A	100%	30	Scope of work include: Construction of concrete drains and culverts; and Stone-Pitching of embankment. The project is 100% completed and awaiting Commissioning and Handing Over
25	Kumo Gully Erosion Site, Anguwan Jauro Sabo, Akko LGA, Gombe State	March, 2017	Ecological Fund Office	6 Months	N/A	100%	28	Scope of work include: Construction of concrete drains and culverts; and Stone-Pitching of embankment. The project is 100% completed. Awaiting commissioning and handing over.
26	Amper Flood Hazards and Erosion Control Works, Tarka LGA	March, 2017	Ecological Fund Office	6 Months	N/A	100%	28	Scope of work include: Construction of concrete drains; Concrete culverts; and Stone-Pitching. The project is 100% completed. Awaiting commissioning and handing over.
27	East of Kumo General Hospital to Jauro Musa Stream Gully Erosion Control Project.	March, 2017	Ecological Fund Office	4 Months	N/A	100%	28	Scope of work include: Site Clearance and earth works; Excavation for side drains and Culverts; Construction of trapezoidal concrete lined drains; Concrete cover Slaps.. The project is 100% completed. Awaiting commissioning and handing over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
28	Flood Control and De-silting of Ogbagba in Oshogbo Township, Osun State	March, 2017	Ecological Fund Office	6 Months	N/A	100%	30	Scope of work include: Dredging and De-silting; Construction of Concrete embankment. The project is 100% completed. Awaiting commissioning and handing over.
29	Abaji Gully Erosion and Flood Control, FCT, Abuja	March, 2017	Ecological Fund Office	6 Months	N/A	100%	28	Scope of work include: Site Clearance; Reclamation of half of the gully; Construction of Road 1; Construction of drainage along Road 1; Provision of Collector drain to connect to the reclaimed gully. The project is 100% completed. Awaiting commissioning and handing over.
30	Erosion & Flood Control at Ifedayo/Boluwadu/Ila in Osun State	May, 2017	Ecological Fund Office	8 Months	N/A	100%	30	Scope of work include: Construction of concrete drains/Culverts; Retaining wall; Earth work; and Asphalt pavement. The project is 100% Completed. Awaiting commissioning and handing over.
31	Erosion Control and Channelization of Okoko River, Oshogbo, Osun State	May 17th , 2017.	Ecological Fund Office	6 Months	N/A	100%	30	Scope of work include: Dredging and De-silting; Construction of Concrete embankment. The project is 100% completed. Awaiting commissioning and handing over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
32	Bagole-Kofare Erosion Control Works, Yola North, Adamawa State.	May, 2017	Ecological Fund Office	6 Months	N/A	100%	30	Scope of work include: Construction of concrete drains/culverts; and Earth work. The project is 100% completed and awaiting Commissioning and Handing Over.
33	Mitigation of Flooding into Uburu Salt Lake And Over 20,000 HA of Rice Farm at Asu-Umunaga, Ubulu, Ebonyi State.	May, 2017	Ecological Fund Office	7 Months	N/A	45%	30	Scope of work include: Dredging; Concrete drains/culverts; and Retaining wall. As at January, 2018, the project is 45% on-going. Challenge: Community disagreement posed a challenge but resolved already with extension granted to the Contractor
34	Amachara Flood And Erosion Control Works, Abia State.	May 3rd , 2017	Ecological Fund Office	7 Months	N/A	100%	28	Scope of work include: Site Clearance and earth work; Retaining wall and drainages; and slope protection. The project is 100% ongoing. The Contractor has been instructed to speed up the work.
35	Contract for Erosion control Works at Makinde way and Environs idimu Lagos State	June 1st ,2017.	Ecological Fund Office	7 Months	N/A	85%	28	Scope of work include: i. Construction of 1,235m Reinforced Concrete Channel. ii. Construction of 2 Culverts; iii. Pavement and Surfacing. Project is 85% on-going.
36	Contract for Erosion and flood control Project Aiyeotoro Community Ondo State	June 1st ,2017.	Ecological Fund Office	7 Months	N/A	100%	30	The scope of work include: i. Construction of 1.2 km Walkway and Drainage; ii. Interlocking Pavement; iii. Construction of 5 Box Culverts. Project is 100% completed. Awaiting commissioning and handing over.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
37	Contract for Erosion and flood control Works in Eruwa, Ibarapa East LGA Oyo State	June 1st ,2017.	Ecological Fund Office	3 Months	N/A	100%	25	Construction of 204m Reinforced Concrete Channel and Construction of 2 Culverts. 100% Completed. Awaiting commissioning and handing over.
38	Contract for Erosion and flood control Works Medical School, Bauchi Town, Bauchi Metropolis LGA Bauchi State	June 1st ,2017.	Ecological Fund Office	6 Months	N/A	100%	28	Scope of work include: i. Construction of 1,777m of Reinforced Concrete Drains with backfilling and Compaction; ii. Construction of 2 Box Culverts. Project is 100% completed and awaiting Commissioning and Handing Over.
39	Contract for Erosion and flood control Works in Tarka and Guma LGA Benue State	June 1st ,2017.	Ecological Fund Office	6 Months	N/A	88%	28	Scope of work include: i. Construction of 982m Drainage; ii. Earthworks; iii. Surfacing Work, iv. Construction of 4 Box Culverts, v. Bridge Works. The project is 88% completed and Ongoing.
40	Jalingo Metropolis (Kofar Fada) Shetima and Kasuwan Yelwa Areas, Turaki A Wards, Taraba State	June 1st ,2017.	Ecological Fund Office	6 Months	N/A	100%	30	Status of work done are: i. Excavation and desilting of all the existing drains and culverts including the drains within the roundabout; ii. Access slabs were provided as required in the BEME; iii. Double Cell Culvert has been constructed; iv. Pot holes and failed part of Shetimma Central Mosque road has been rehabilitated. The project has achieved 100% completed. Awaiting commissioning and handing over.
44	Erosion Control Works in Uvu, Askira Uba LGA, Borno State.	June 1st ,2017.	Ecological Fund Office	6 Months	N/A	100%	30	Scope of work include: Site Clearing; Construction of Drainages of various sizes & dimensions; Culverts, Slabs and Road Improvements Works etc. The project is 100% completed. Awaiting commissioning and handing over

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
45	Tambuwal-Dogondaji Erosion Works, Sokoto State	June 1st ,2017.	Ecological Fund Office	7 Months	N/A	100%	30	Scope of work include: Site Clearing; reclamation works and construction of drains at Bashire, Dogondaji and Road improvement works at Jabo town. The project is 85% ongoing.
46	Odolu Community Soil Erosion and Flood Control Project, Kogi State	June 1st ,2017.	Ecological Fund Office	12 Months	N/A	100%	30	Scope of work include: Construction of concrete drains; dredging; Stone-Pitching of the bridge area. The project is 100% completed and awaiting Commissioning..
47	Gully Erosion and Flood Control, Idumu Osigbudu Street, Delta State.	June 1st ,2017.	Ecological Fund Office	6 Months	N/A	100%	28	Scope of work include: Site clearing and earth works; Drainages and Culverts; Road Improvement works and Surface dressing. The project is 100% completed and awaiting commissioning and handing over
48	Gully Erosion and Flood Control Works at Akpene Eket and Its Environs, Akwa Ibom State.	June, 2017.	Ecological Fund Office	7 Months	N/A	100%	30	Scope of work include: Site Clearance & earth works; Culverts and Drains as well as Pavement Surfacing. The project is 100% completed. Awaiting commissioning and handing over.
49	Magama LGA Erosion and Flood Control Project, Niger State.	June,2017.	Ecological Fund Office	9 Months	N/A	89%	30	Scope of work include: Construction of type 1 rectangular drains at Ibeto; Construction of 2 drains (Trapezoid 2.3m base) at Ibeto; Construction of type 1 drains at Salka; and Construction of a 3 cell box culverts at Busra. The project is 89% Ongoing.
50	Soil Erosion Control and Road Improvement Works, Yalenguruza, Gombe, Gombe State.	June , 2017.	Ecological Fund Office	6 Months	N/A	90%	30	Scope of work include: Site Clearing and earth works; 16m Culvert of 3m high; 4 No. side drains and Road improvement including retaining wall etc. The project is 90% ongoing.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITTLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
51	Soil Erosion and Flood Control Project at Agenebode/Fugar Erosion Site, Edo State	June, 2017.	Ecological Fund Office	5 Months	N/A	100%	28	Scope of work include: Site clearing; Earth works; Concrete drainages, culverts and Slabs; Agronomic measures; and soil conservation. The project is 100% completed and awaiting Commissioning and Handing Over.
52	Flood, Channelization and Reconstruction of Failed Structures along Ijebu-Ode/ Ilese Road Via Owa River, Ogun State	June ,2017.	Ecological Fund Office	6 Months	N/A	50.16%	30	Scope of work include: Channelization of River Owa; Reconstruction of failed structures; and Road Construction. The project was Stopped at 50.16% completion by Ogun State government.
53	Abaji Gully Erosion and Flood Control Works, Phase II, FCT. Abuja	June ,2017.	Ecological Fund Office	6 Months	N/A	100%	30	Scope of work include: Site Clearance; Reclamation of part of the gully; Construction of Road 2; Construction of a reinforced concrete drain along the Road 2; Provision of Collector drain to connect to the reclaimed gully. the project is 100% completed. Awaiting commissioning and handing over.
54	Jikwoyi Erosion and Flood Control Works, AMAC	October, 2017	Ecological Fund Office	4 Months	N/A	100%	28	Scope of work include: Site Clearance; Earth works; Culverts & Line Drains; Pavement and Surfacing. The project is 100% completed. Awaiting commissioning and handing over.
55	Gully Erosion/Flood Control & Road Improvement works at Sokale Community, Dutse Alhaji, Bwari Area Council, FCT	October 11th, 2017	Ecological Fund Office	3 Months	N/A	100%	25	Scope of work include: Site Clearing and earth works; Culverts and Drains; and Pavement and Surfacing. The project is 100% completed and awaiting commissioning and handing over

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
56	Erosion Control Works along Bauchi-Ningi Road Junction to the Main Campus of Abubakar Tafawa Balewa University, Bauchi State	October, 2017	Ecological Fund Office	4 Months	N/A	65%	30	Scope of work include: Site Clearance and Earth work; Concrete works as Drains and Culverts; Stone-Pitching; and Pavement Surfacing. The project is 65% ongoing.
57	Burga - Gwammadaji Flood and Erosion Control Works, Bauchi State	October, 2017.	Ecological Fund Office	6 Months	N/A	65%	26	Scope of work include: Site Clearing; Construction of culverts; Earth works; Drains and Concrete walls; Pavement and Surfacing. The project is 65% Ongoing.
58	Stream Erosion Control at Chief Ogungbo Road One River along Olabisi Onabanjo University Road, Ago Iwoye, Ijebu North LGA, Phase 1, Ogun State	October, 2017.	Ecological Fund Office	7 Months	N/A	80%	30	The Scope of work include: i. Site Clearance/Preparation; ii. Earthworks and Excavation; iii. Dredging; iv. Channel Preparation/Rehabilitation works. The project is 80% ongoing.

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
59	Rehabilitation of Eroded Road and Drain in Apo Resetlement, Apo District, AMAC, Abuja	October 2017	Ecological Fund Office	5 Months	N/A	100%	26	Scope of work include: i. Site Clearing and Earthworks ii. Culverts and Drains iii. Road Works; and iv. Auxillary Works The project is 100% completed. Awaiting commissioning and handing over.
60	Flood and Erosion Control at Karshi Town in FCT, Abuja	October 2017	Ecological Fund Office	6 Months	N/A	100%	28	Scope of work include: i. Site Clearing and Earthworks; ii. Culverts and Drains; iii. Pavement and Surfacing The project is 100% completed and awaiting commissioning
61	Gully Erosion/Flood Control and Road Improvement Works at Durumi Mpape, FCT. Abuja	October 2017	Ecological Fund Office	3 Months	N/A	100%	25	Scope of work include: i. Site Clearing and Earthworks; ii. Culverts and Drains; iii. Road Improvement Works

THE STATUS OF IMPLEMENTATION OF APPROVALS BY THE ECOLOGICAL FUND OFFICE TENDERS BOARD FROM MAY 2015 TO DECEMBER 2017

SN	PROJECT TITLE	DATE OF APPROVAL	USER AGENCY	CONTRACT & PROCUREMENT DURATION	FUNDS ACCESSED BY THE PROJECT (%)	STATUS OF IMPLEMENTATION (%)	NO OF JOBS CREATED SKILLED/ UNSKILLED	REMARKS (PROSPECTS OF COMPLETION)
62	Ratification of the Award of Contract for the Reconstruction of Damaged Culverts and Road Improvement Works at Kapwa Road, Lugbe, Abuja	October 2017	Ecological Fund Office	3 Months	N/A	100%	28	Scope of work include: i. Site Clearing and Earthworks; ii. Culverts and Drains; iii. Road Improvement Works; iv. Pavement and Surfacing The project is 100% completed and awaiting commissioning and handing over
63	Contract for the Reconstruction of 3,125m2 Collapsed Boundary Fence at Federal Government College, Malali, Kaduna State	October 2017	Ecological Fund Office		N/A	100%	25	Scope of work include: i. Site Clearing and Earthworks; ii. Concrete and Block works; iii. Reinforcement and Formworks The project is 100% completed and awaiting commissioning.
64	Reconstruction of Damaged Culvert and Road Improvement Works at Saburi, AMAC, FCT. Abuja	October 2017	Ecological Fund Office	4 Months	N/A	100%	28	Scope of work include: i. Site Clearing and Earthworks; ii. Culverts, Drains and Concrete works; iii. Pavement and Surfacing iv. The project is 100% completed and awaiting commissioning and handing over
